



Filter fastening and removal: now included in the CAD

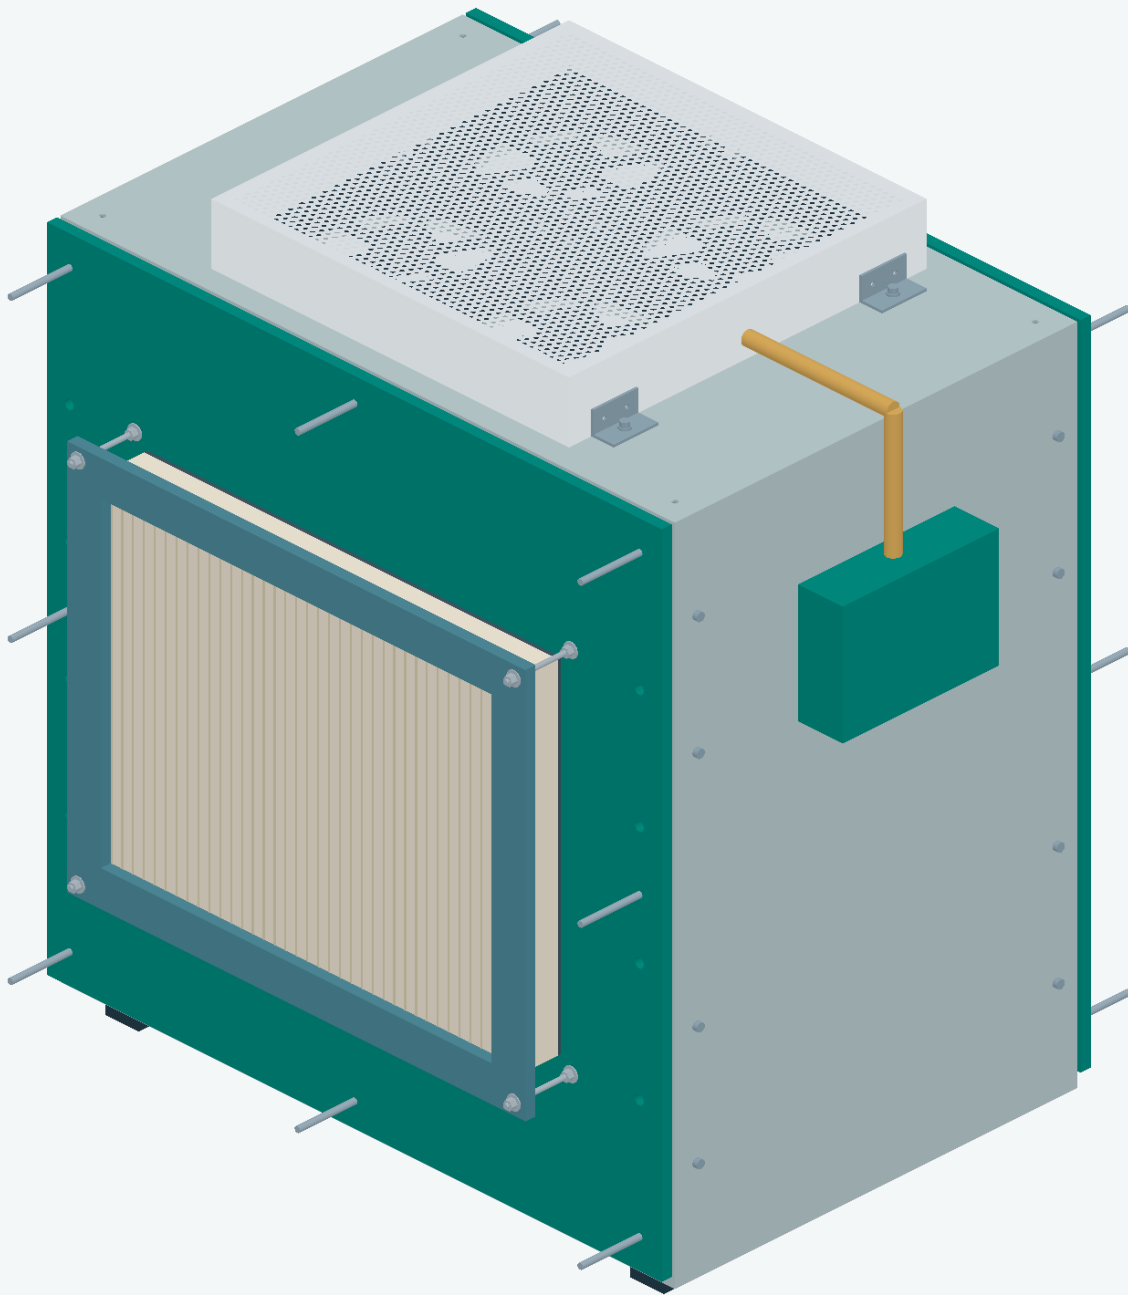

FRONT STUD STACK / global y coordinates (mm); rear mirrored about y=180

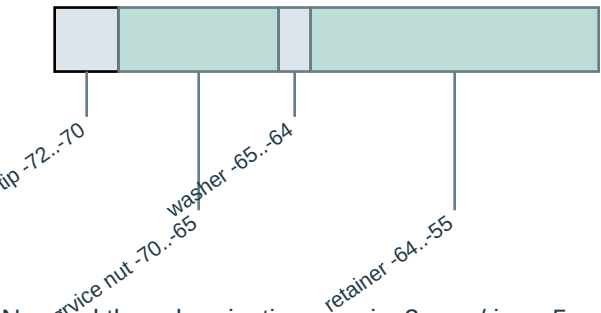

Normal thread projection: service2 mm / inner5 mm / ledge6 mm. Two-pitch1.4 mm comparison is an assumption, not a release criterion.

Original R02 preserved. Sources and reproducible commands: README.md beside this sheet. No prices, availability or physical results claimed.

DETECTED: 229 valid CAD objects; 13644 changed-part pair checks with no modeled clashes. Native reopen and STEP volume checks pass.

CHANGED: eight 70 mm rod envelopes replaced with proposed M4 x80 studs. Four ledge screws now have25 mm under-head length and modeled cap heads. Added28 nuts and32 metal backing washers.

SERVICE CHECK: after removing the four service nuts, washers and retainer on each side, the filter has a nominal200 mm straight outward travel without collision. Isolate power and wait for fans to stop before access; protective access controls remain unresolved.

ASSUMPTIONS: nut7 mm across flats x5 high; washer12 OD x4.3 ID x1; installed sealing washer1 mm. Gasket compression, filter border, tool/hand access and manufacturing tolerances are not verified.

NOT RELEASED: this check does not establish strength, leak tightness, protection from moving fans or restart safety. Inherited M5 hardware remains incomplete. Indoor experimental use only; physical prototypes:0.

